AcadMate

Sprint 2 Review

Student progress and advisor approvals

November 7, 2026

AGENDA

Today’s review

01 **Project and team**

People, MVP and design

02 **Scope and working software**

Backlog, screenshots and test results

03 **Metrics and next work**

Task log, retrospective and proposed Sprint 3

04 **Live application**

Student, advisor search and approval flow

TEAM

Team roles and introductions

Team member	Role in working agreement
Tafadzwa Nhesvure	Product Owner / AI-ML Developer
Pranali Dukhande	Scrum Master / Backend Developer
Datta Vardhan Reddy Kontham	Database Manager / Backend Developer
Pragnan Chintu Gulivindala	Tester
Liangxian Li	Backend Developer
Lyno Chihwehwete	Frontend Developer / LLM Developer
Saisai Hu	Developer

Academic advising for three users

User	Need	Product response
Student	Understand remaining requirements	Degree audit, credits and course plan
Faculty advisor	Review a student’s plan	Advisee records and approval queue
Administrator	Maintain reliable academic data	Accounts, catalog and data management

The MVP supports a complete advising flow

Sprint 1 documented foundation

Authentication and role access

UI wireframes

Academic data preparation


Current verified MVP

Student degree progress

Advisor search and student records

Approval visible in the student plan

The local stack separates UI, API and data

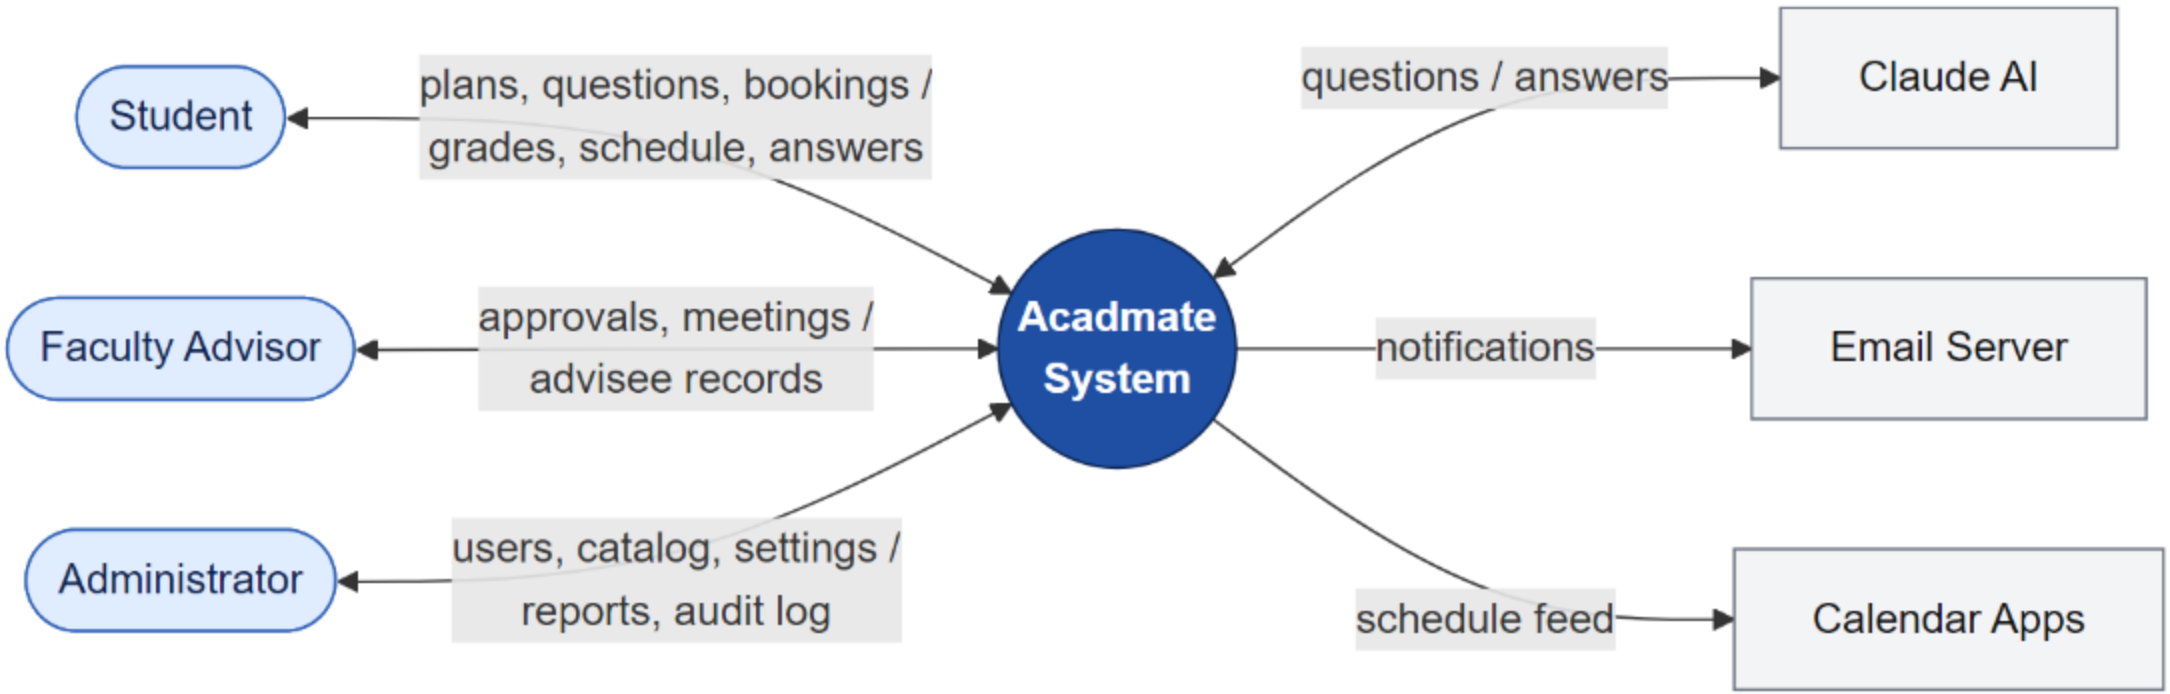

React + Vite **FastAPI + SQLAlchemy** **PostgreSQL**

Degree audit works, model inference is blocked

Main application

Requirement group allocation

Earned and remaining credit totals

Rule based advisor attention flags

Risk research branch

Logistic regression, 16 features

Sigmoid calibration pipeline

Inference blocked by two missing files

SPRINT 2 SCOPE CANDIDATE 1 OF 2

Advisor and degree progress backlog


Item	Acceptance criterion from planning	Current evidence
S2-01 Authentication	Required authentication flow works and is tested	Verified locally
S2-02 Advisor UI	Advisor profile screens are complete and reviewed	Flow verified PO review pending
S2-03 Integrations	Required advisor integrations work end to end	Partial
S2-04 Requirements	Requirement groups show correct completion status	Verified locally
S2-05 Credits	Earned and required credits are calculated correctly	Verified locally

SPRINT 2 SCOPE CANDIDATE 2 OF 2

Risk and AI foundations remain open

Item	Acceptance criterion from planning	Current evidence
S2-06 Training data	Dataset is cleaned, documented and ready for training	Branch code Training not rerun
S2-07 Baseline model	Model trains and produces risk predictions	Blocked Frozen files missing
S2-08 Risk thresholds	Thresholds documented and linked to model outputs	Partial Policy unapproved
S2-09 SHAP	Predictions have interpretable SHAP explanations	No evidence
S2-10 Knowledge	Approved sources are ingested and retrievable	No evidence

Students can see remaining degree work

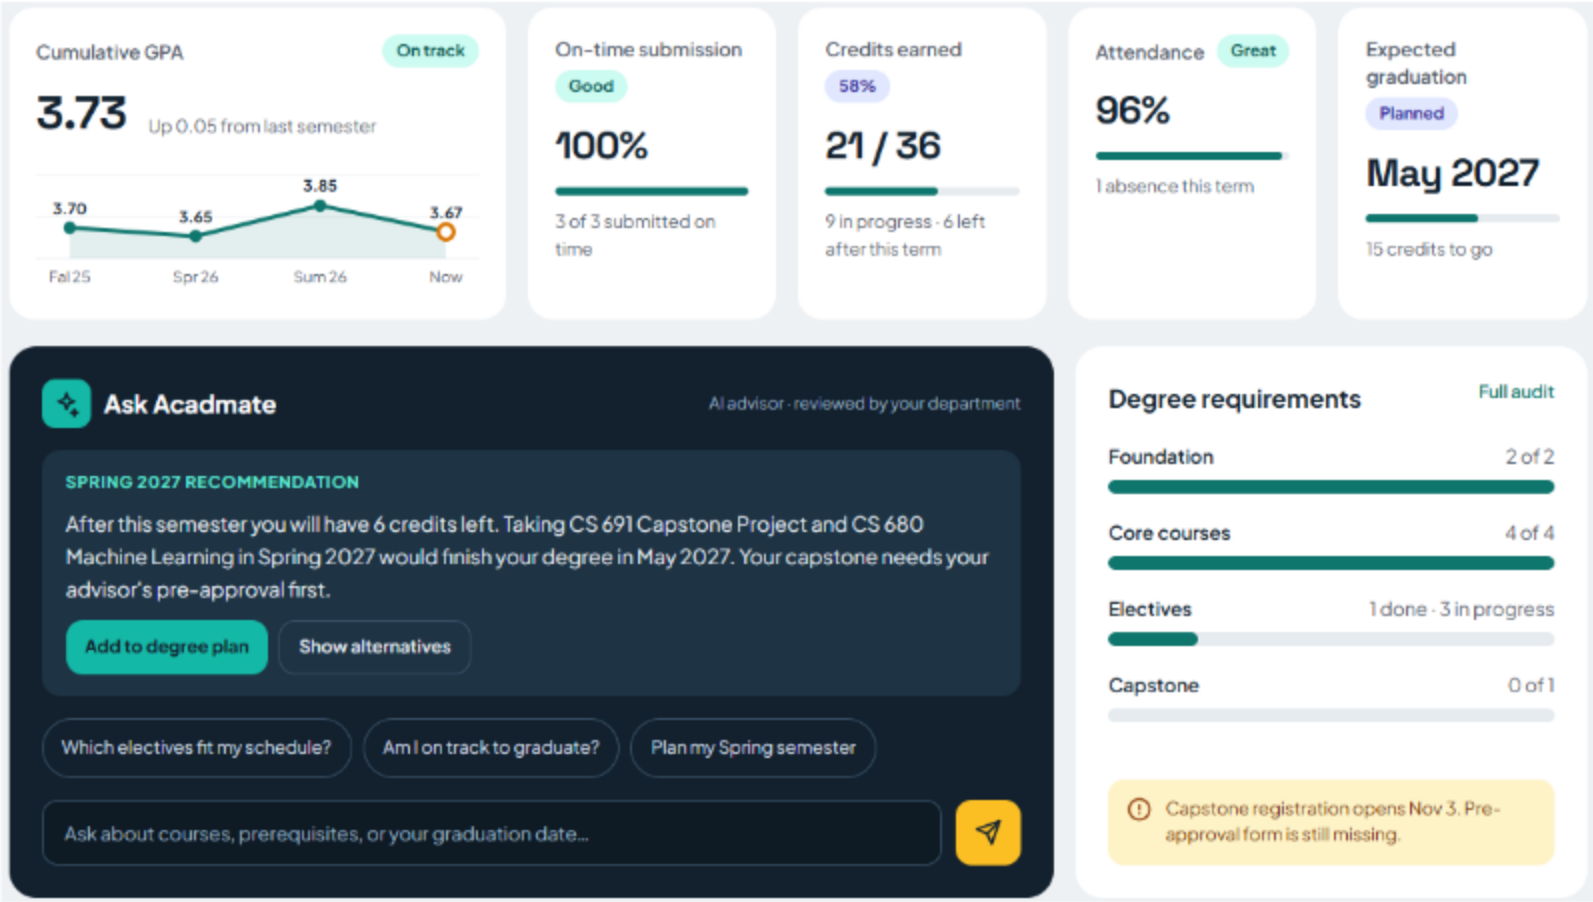

21 / 36


credits earned

9 in progress

6 left after term


SEARCH FIX VERIFIED NOVEMBER 7

Advisor name search now returns Amara

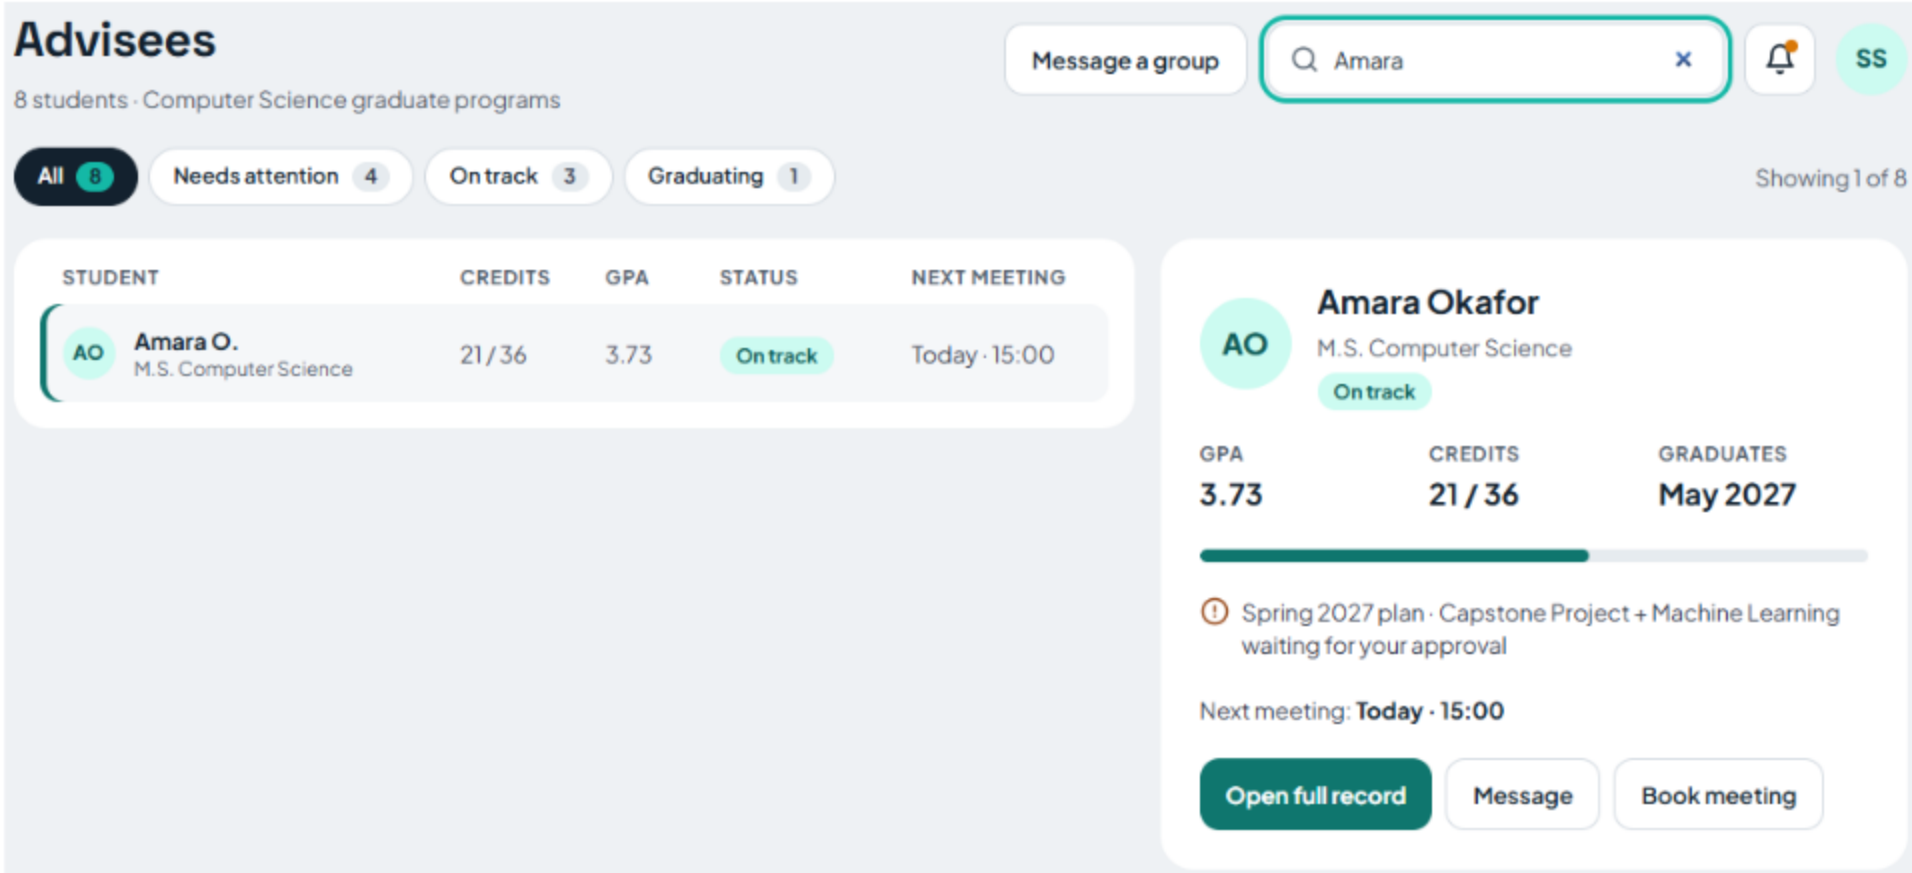

VERIFIED APPROVAL ROUND TRIP

Advisor approval reaches the student plan

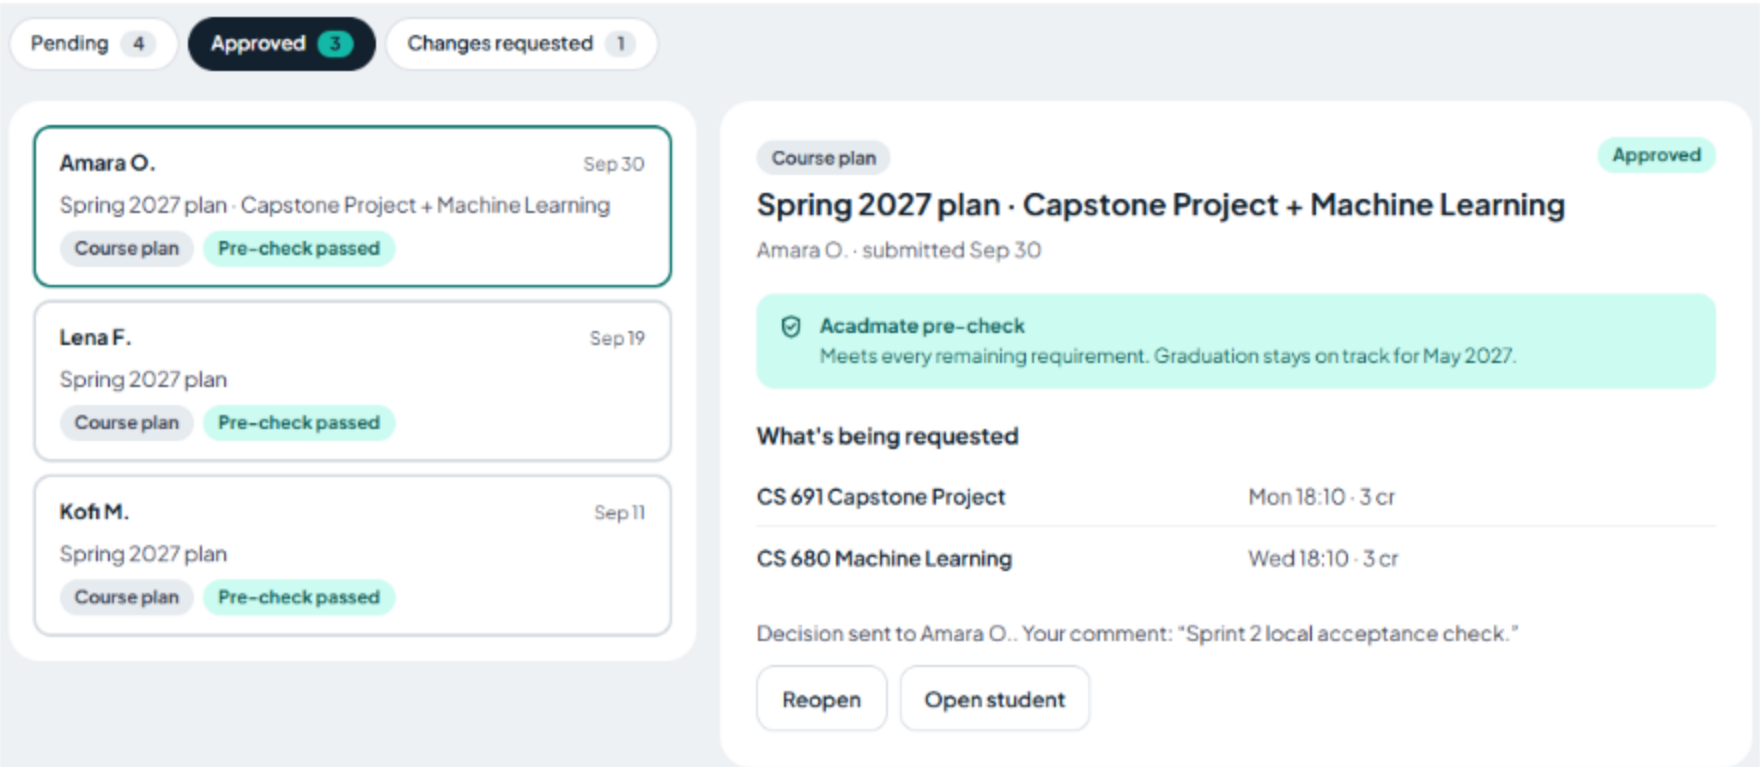

Request 1709

CS 691
Capstone Project

CS 680
Machine Learning


Tests support the demonstrated core

API / test	Role and expected behavior	Evidence
Student degree audit	Student sees earned and required credits	21 earned / 36 required
Advisor advisee query	Advisor searches Amara	1 result from 8
Approval request 1709	Advisor approves, student refreshes	2 courses Approved
Advisor dashboard access	Student attempts advisor data access	403 Forbidden

353 backend tests passed

7 / 7 search fix checks passed

The research UI reports “Not scored”

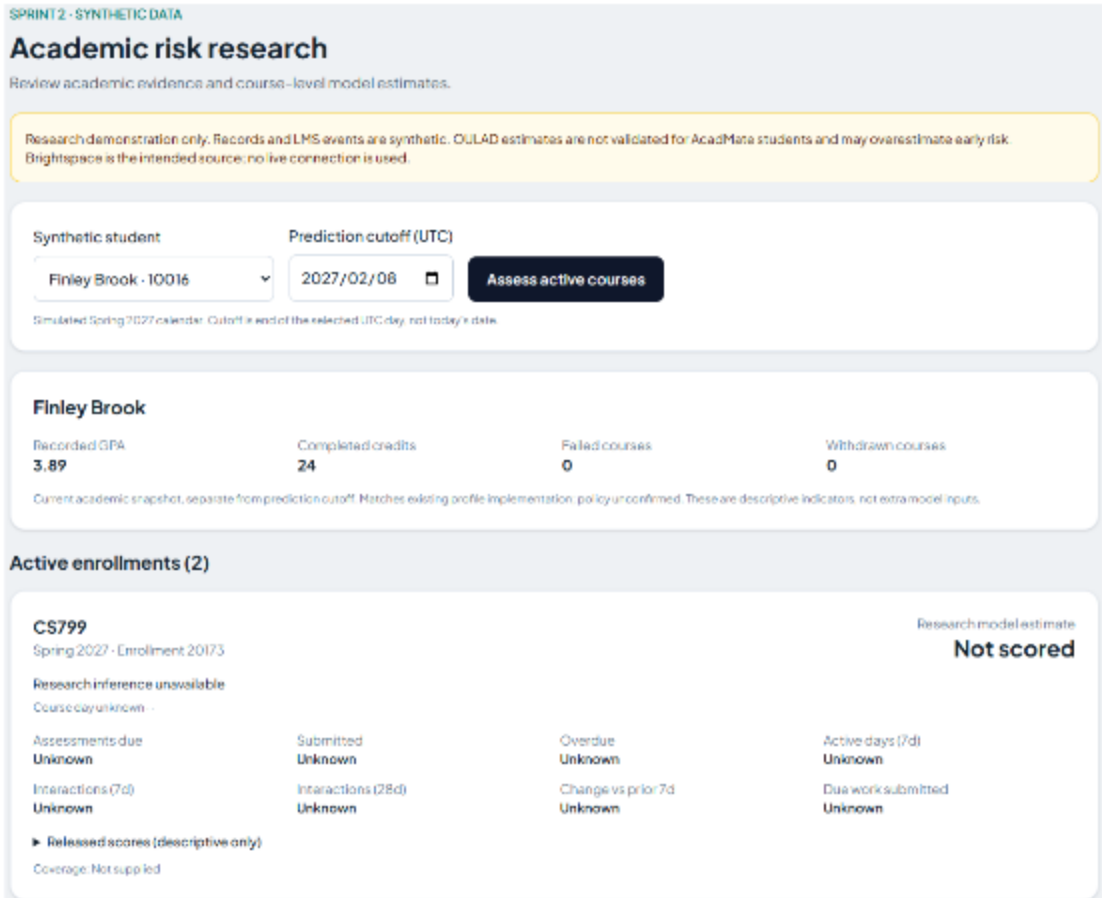

100 students
800 enrollments


Synthetic research data

Two frozen artifacts missing

No model probability available


The task log records 26 Sprint 2 points

Recorded velocity, points

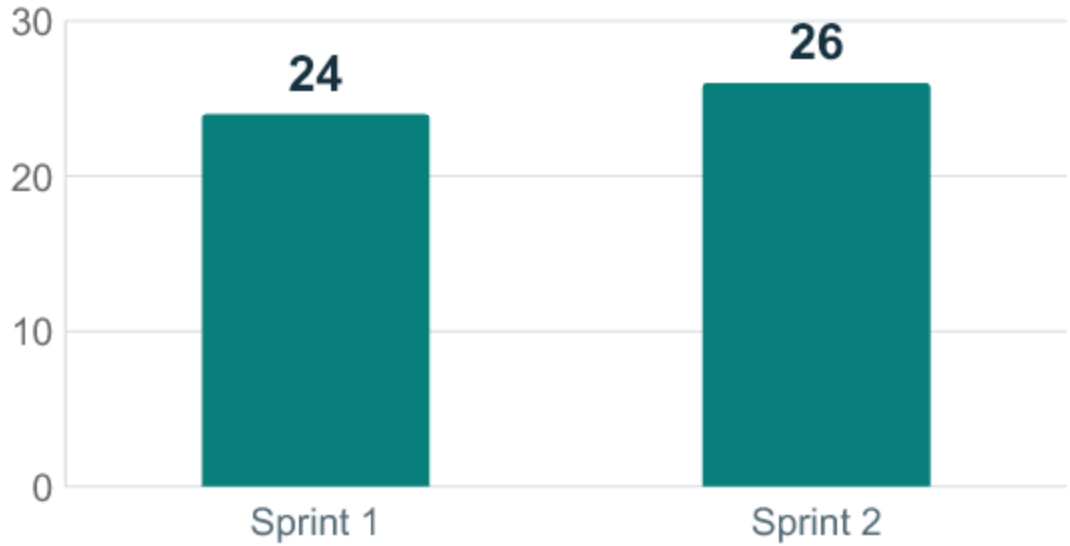

Average: 25 points, excluding Sprint 0


Recorded completion ratio

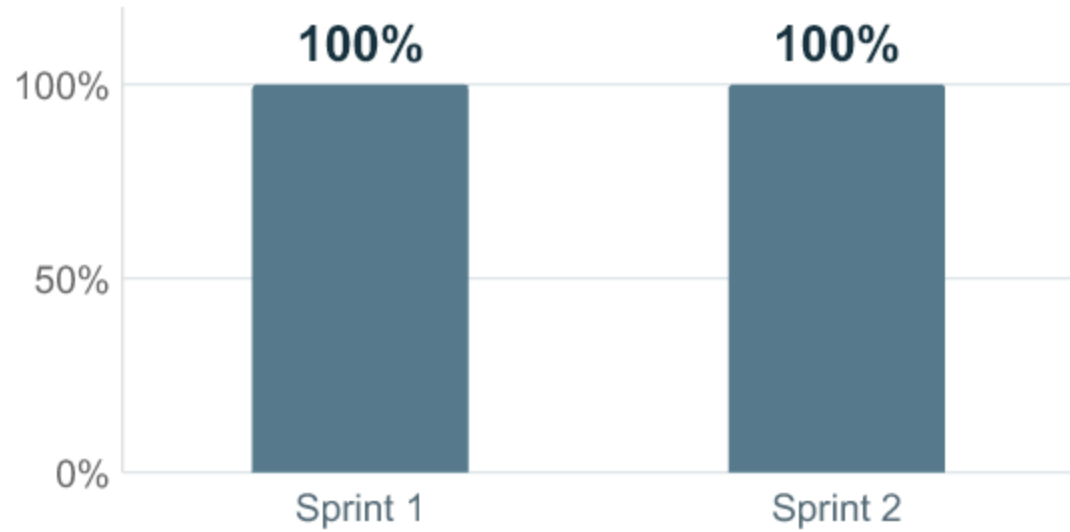

24/24 and 26/26, average 100%

RECONSTRUCTED CURRENT BURNDOWN

Sprint 2 work closed near the recorded end

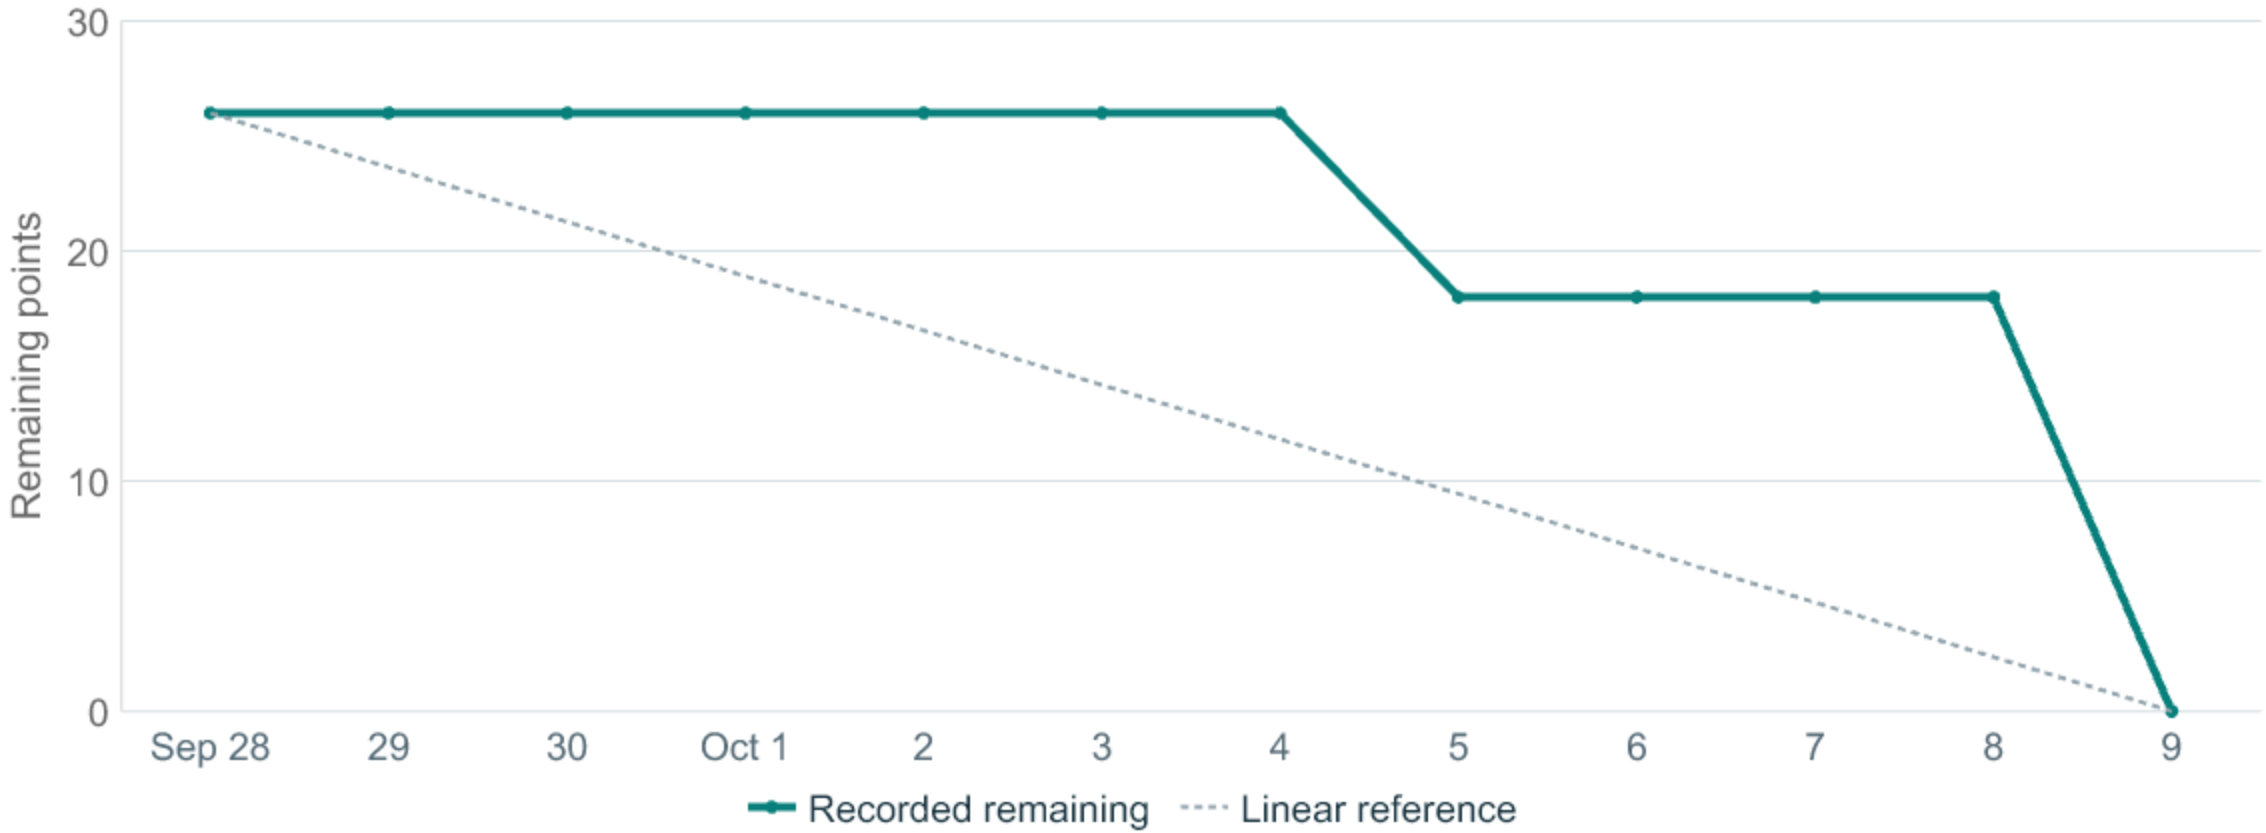

Retrospective actions address observed gaps

Observed issue	Proposed action	Acceptance check
Shared header search broke	Add search behavior to UI review checklist	Match, clear and refresh pass
Model files absent	Owner hands off frozen files and manifest	Both SHA-256 checks match
Scope documents disagree	PO confirms stories, points and dates	One approved Sprint 2 record

SPRINT 3 PROPOSAL

The next sprint needs a confirmed backlog

Candidate priority	Proposed item	Acceptance before completion
1	Confirm scope and carryover	PO approves one backlog and estimates
2	Restore frozen model artifacts	Hashes match and inference cases pass
3	Approve risk outreach policy	Thresholds map to agreed advisor actions
4	Complete explainability and retrieval	SHAP evidence and approved-source tests

APPLICATION DEMONSTRATION

The live demo follows the advising workflow

Time	Live action	Expected result
0:00–0:50	Student dashboard and Degree plan	21/36 credits and remaining groups
0:50–1:40	Advisor searches Amara	1 of 8 advisees, full record opens
1:40–3:10	Approve request 1709, refresh student	Both planned courses show Approved
3:10–4:00	Reopen request and optionally show risk	Pending restored, research Not scored

APPENDIX A1

Product backlog covers eleven areas

Item	Product backlog area	Recorded scope
PB-01	Authentication and access	Login, passwords and role permissions
PB-02	Data import and management	Student/LMS records, validation and error reports
PB-03	Student dashboard	Academic progress, risk and recommendations
PB-04	Admin dashboard	Accounts, performance and system settings
PB-05	Advisor dashboard	Records, progress and pending interventions
PB-06	Risk prediction and explainability	Model estimates and contributing factors

Product backlog continues beyond this sprint

Item	Product backlog area	Recorded scope
PB-07	Recommendations and interventions	Tutoring, study plans and follow-up tracking
PB-08	Conversational AI and RAG	Answers grounded in approved university sources
PB-09	Integration and notifications	SIS/LMS interfaces and academic alerts
PB-10	Testing, security and performance	Functional, usability, security and load checks
PB-11	Deployment and feedback	Production configuration, guides and user feedback

The working agreement defines completion

How the team works

Zoom discussions, WhatsApp updates

GitHub code and Wiki documentation

Two meetings each week

Definition of Done

Acceptance criteria and tests pass

Peer review and integrated UI/API/data

Documentation and PO verification

APPENDIX C1

Repository architecture documents the layers

Layer	Repository components	Evidence boundary
Browser	React pages, AppShell, API client	Current advisor flow verified
API	FastAPI routers and role checks	Main backend regression passed
Business services	Degree audit, plans and approvals	Approval round trip verified
Storage / providers	SQLAlchemy, PostgreSQL, external adapters	Local DB verified, providers unverified

The ER model connects students to accounts

STUDENTS		
int	student_id	PK
int	user_id	FK
int	program_id	FK
string	expected_graduation	


Student entity detail

student_id identifies the student


user_id links the account

program_id links the degree program

Sign in creates a server session

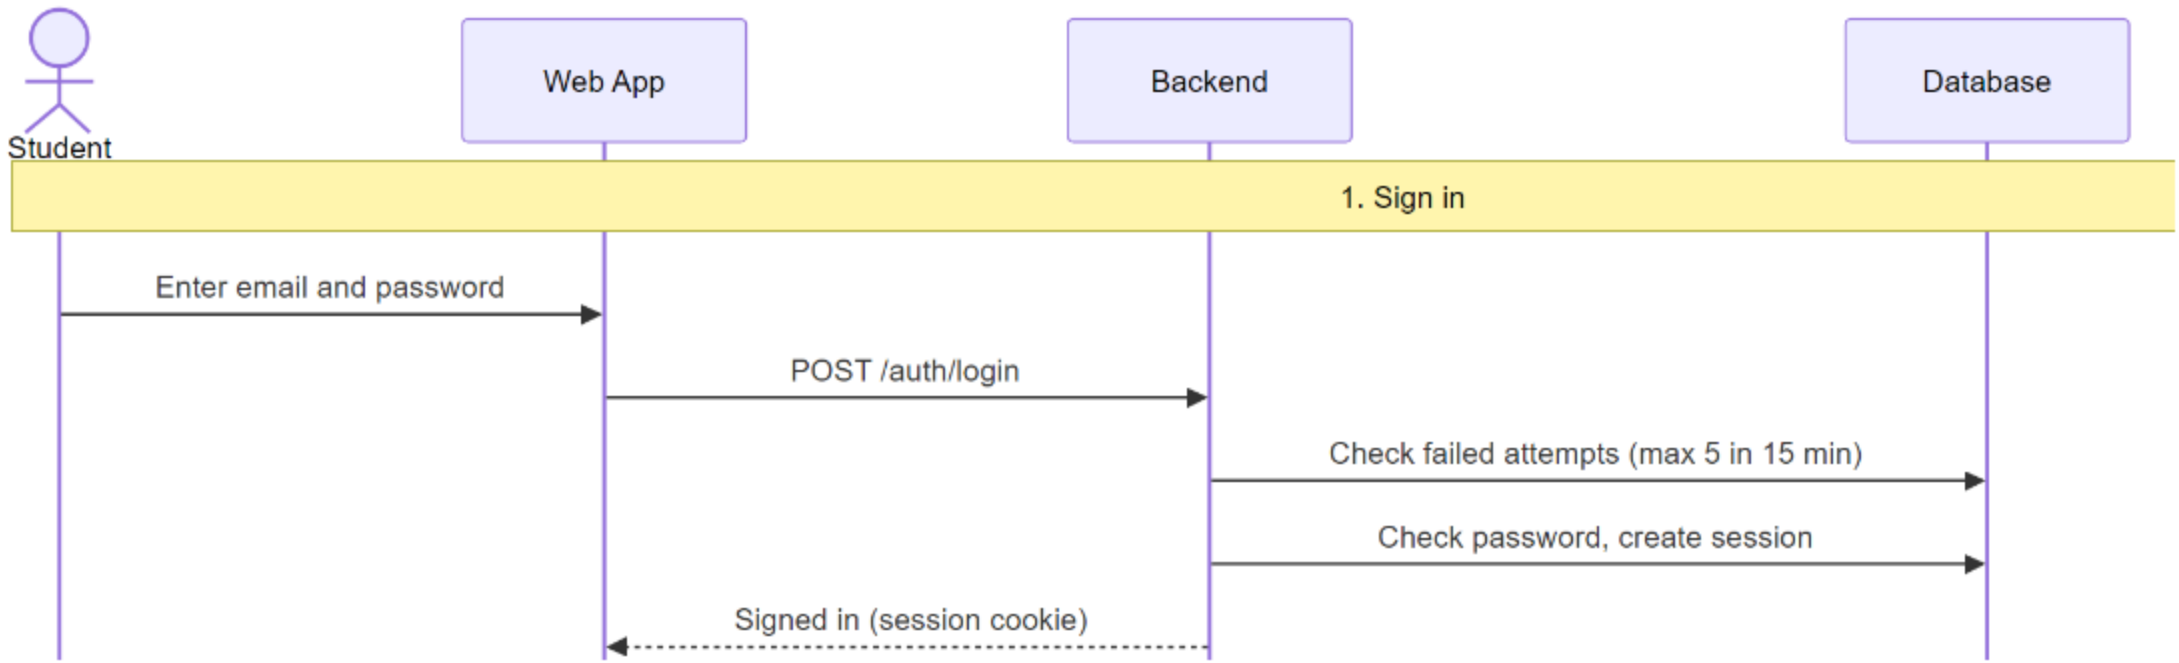

The state model complements runtime checks

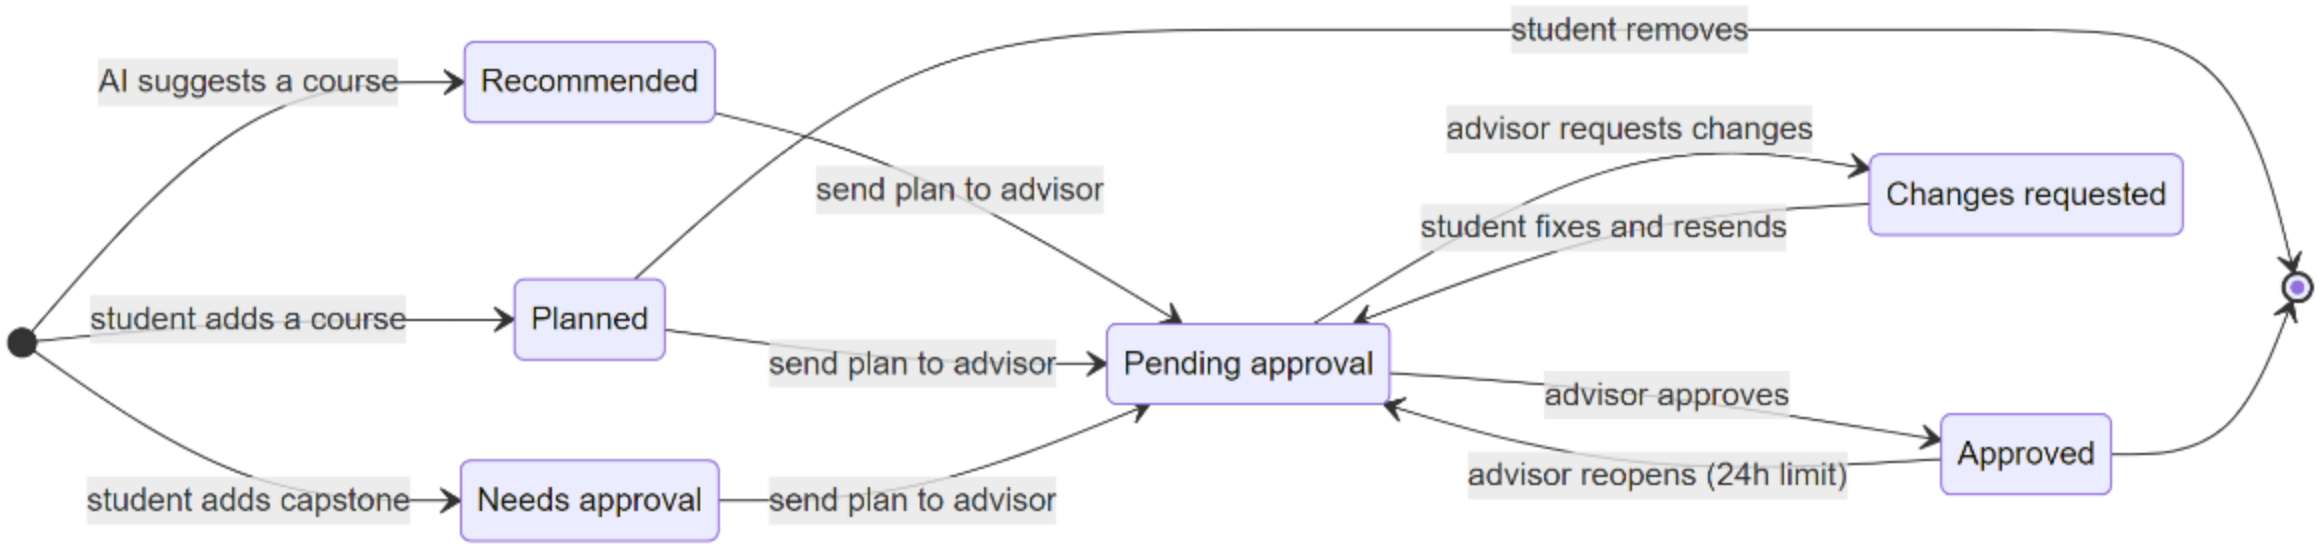

APPENDIX D

Model delivery requires the original artifacts

Required artifact	Current state	Acceptance before use
logistic_regression.joblib	Missing	Match frozen SHA-256
calibration_maps.joblib	Missing	Match frozen SHA-256
Supporting frozen source files	6 verified	Retain matching configuration
Inference acceptance cases	Blocked by missing files	Restore artifacts and rerun

Historical burndowns require comparable timing

